

# Homewood High – Phase 1: Building Addition

PROGRAM MANAGER: Hoar Program Management (HPM)  
 ARCHITECT: Goodwyn Mills & Cawood (GMC)  
 CONTRACTOR: MJ Harris Construction


## SCOPE OVERVIEW:

New 2 Level Classroom Addition, New Sports Pavilion Addition, New Fine Arts Pavilion Addition

CONTRACT RECAP:	Start	Executed CO	Projected Finish
• Contract Amount	\$29,500,000	\$150,569	\$29,650,569
• Contract Schedule	10/2/18	*Pending +31 Days	02/2020 + Pending Time



## Progress Status: In Construction

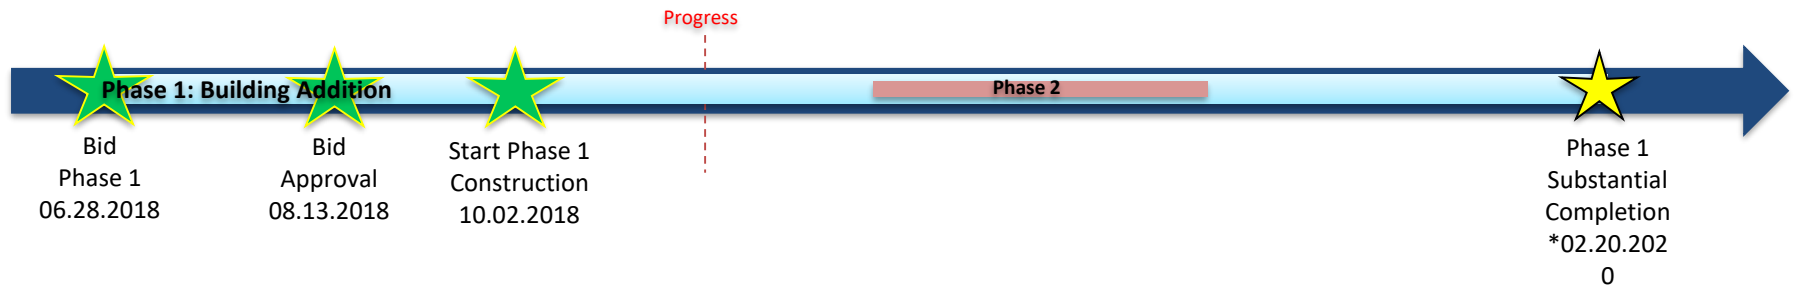

### ACHIEVEMENTS:

- ✓ Phase 1 Bid
- ✓ Bid Approval
- ✓ Value Analysis
- ✓ Notice of Award
- ✓ Start Construction

### NEXT STEPS:

- Site Utilities
- Foundations
- Structure
- Dry-In
- Finishes

### CLOSURES & SHUTDOWNS:

- N/A



# Homewood High School – Phase 1 Building Addition

## Progress Photos – Phase 1

New Storm Structures



Site Grading

