

Homewood High – Phase 1: Building Addition

PROGRAM MANAGER: Hoar Program Management (HPM)
 ARCHITECT: Goodwyn Mills & Cawood (GMC)
 CONTRACTOR: MJ Harris Construction


SCOPE OVERVIEW:

New 2 Level Classroom Addition, New Sports Pavilion Addition, New Fine Arts Pavilion Addition

CONTRACT RECAP:	Start	Executed CO	Projected Finish
• Contract Amount	\$29,500,000	\$1,643,015	\$31,143,015
• Contract Schedule	10/2/18	112	06/27/20 *8 contractual weather days pending



Progress Status: In Construction

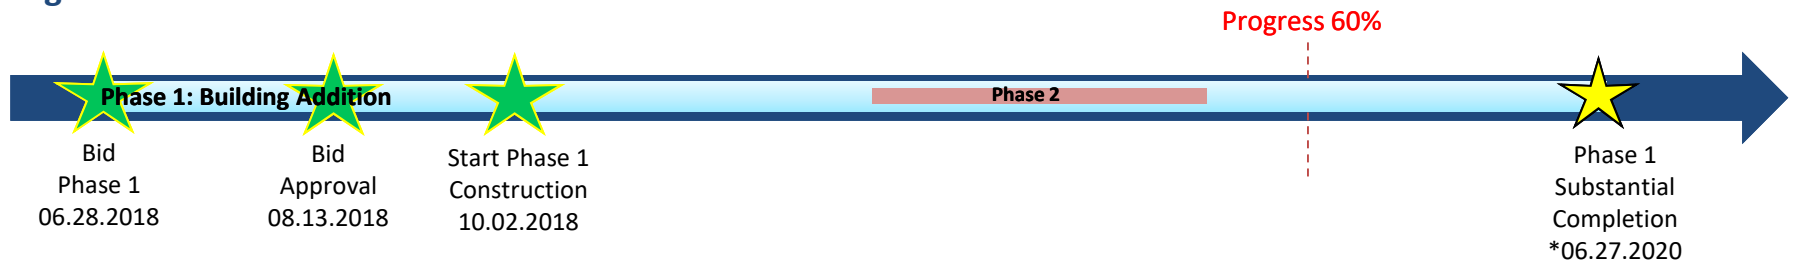

ACHIEVEMENTS:

- ✓ Athletics – Roofing
- ✓ Athletics – Drywall
- ✓ Atrium Steel
- ✓ Arts – Framing
- ✓ Arts – Rough In

NEXT STEPS:

- Classrooms – Roof Joist & Deck
- Arts – Roofing
- Arts – Drywall
- Athletics – Overhead Inspection

CLOSURES & SHUTDOWNS:

- Spring Break – Tie-In to existing school loop water mechanical system
- Existing Roof Drain replacements and routing (after hours & weekends)



Homewood High School – Phase 1 Building Addition

Site/Floorplan Overlay



Homewood High School – Phase 1 Building Addition

Progress Photos – Phase 1

Athletics – Exterior Skin



Athletics - Concourse



Athletics – Trophy Case Framing



Homewood High School – Phase 1 Building Addition

Progress Photos – Phase 1



Arts – Exterior Skin



Theater – AV Booth Framing



Homewood High School – Phase 1 Building Addition

Progress Photos – Phase 1

New Atrium Steel



Classrooms – Joists & Decking

