


Homewood High – Phase 2: Interior Renovation

PROGRAM MANAGER: Hoar Program Management (HPM)
 ARCHITECT: Goodwyn Mills & Cawood (GMC)
 CONTRACTOR: TBD

SCOPE OVERVIEW:


Expanded Dining, Serving & Kitchen Modifications, Repurposed Areas: Media Center (Collaboration Space/ Learning Hub), Interior Student Flow Improvements, Science Lab upgrades, weight room conversion.

CONTRACT RECAP:	Start	Executed CO	Projected Finish
• Contract Amount	TBD	0	\$4.9MM
• Contract Schedule	01/2019	0	08/2019

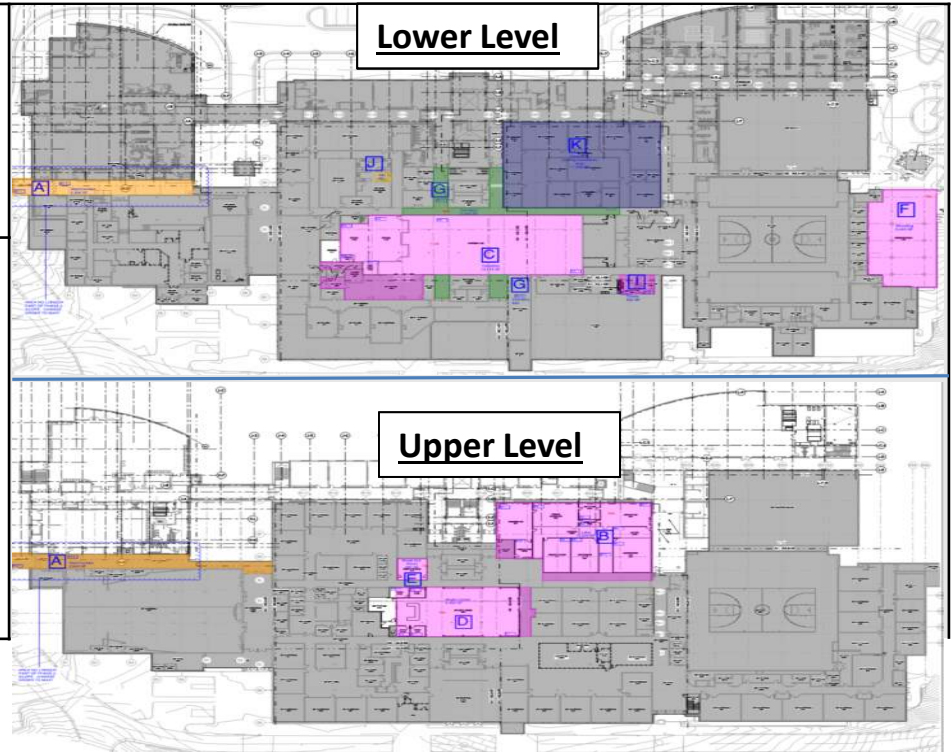

Progress Status: In Design

Progress



ACHIEVEMENTS:

- ✓ Design Development Drawing Submission to Alabama Building Commission – Ph 2

NEXT STEPS:

- Advertise for Bid –Ph 2
- DD Budget Check - Ph 2
- CD/ Final Drawing Submittal - Ph 2
- CD/ Final Budget Check – Ph 2
- Phase 2 Bid

CLOSURES & SHUTDOWNS:

- N/A

