

Homewood Middle School

PROGRAM MANAGER: Hoar Program Management (HPM)
 ARCHITECT: Goodwyn Mills & Cawood (GMC)
 CONTRACTOR: Murray Building Company

SCOPE OVERVIEW:

Summer 2018 Scope:

6th/7th/8th Classrooms/Repurposed Rooms, Additional Office Space, Secure Entry Modification, Build-out new Choral Room (Old Wrestling/Cheer Room), Repurpose Fine Arts to Band Room.


Remaining Scope:

New Multi-Purpose Room Addition, Wrestling & Cheer move to new Multi-purpose Addition



CONTRACT RECAP:	Start	Executed CO	Projected Finish
• Contract Amount	\$2,129,675	\$178,071	2,307,746
• Contract Schedule	May 25, 2018	TBD	Jan. 24, 2019

Progress Status:

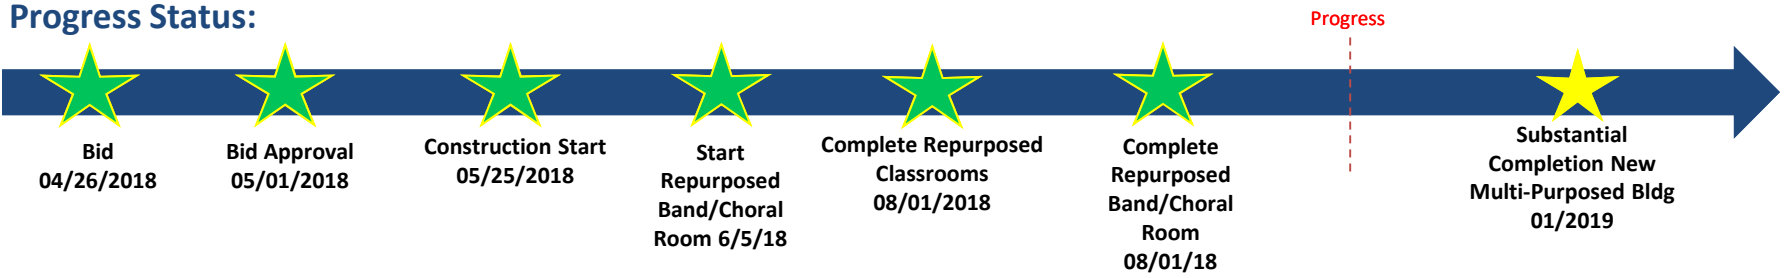

ACHIEVEMENTS:

- ✓ Start Construction
- ✓ Complete 6 additional classrooms
- ✓ Complete Band & Choral Renovations.
- ✓ Addition Structure
- ✓ Finish Secure Vestibule
- ✓ Addition Roofing

NEXT STEPS:

- Addition Interiors
- Addition Punch Lists
- Addition Substantial Completion

CLOSURES & SHUTDOWNS:

- Practice Gym – Half Court removed due to water damage: Fix anticipated by 01/01/19

