

Program Wide Building Automation System


PROGRAM MANAGER: Hoar Program Management (HPM)
 ARCHITECT/ ENGINEER: Bernhard TME
 CONTRACTOR: Alabama Controls, Inc.

SCOPE OVERVIEW:

New Enterprise Server System and Software, New Equipment Level Controllers at all schools and facilities to include All Elementary Schools, Middle School, High School, Waldrop Stadium, and Board of Education Office.

CONTRACT RECAP:	Start	Executed CO	Projected Finish
• Contract Amount	\$1,132,000	\$35,838	\$1,167,838
• Contract Schedule	May 7, 18	TBD	February 4, 19

Example

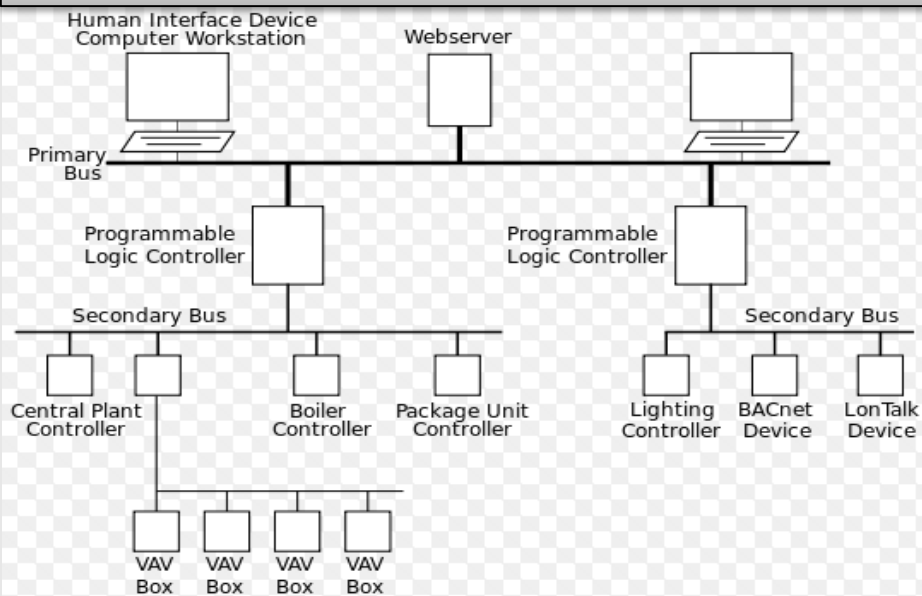

Progress Status: Substantially Complete



ACHIEVEMENTS:

- ✓ Bid
- ✓ Bid Approval
- ✓ Contract Execution
- ✓ Pre-construction Conference
- ✓ Issue Notice to Proceed
- ✓ Start Construction
- Commissioning
- Training

NEXT STEPS:

- Commissioning
- Training
- Close-out

CLOSURES & SHUTDOWNS:

- N/A

